

Parking Lot 6 Solar Powered Generating Photovoltaic System

Irvine Valley College


South Orange County Community College District




Bi-Weekly Progress Update No.4 February 15 through February 28, 2021

PROJECT STATUS:

- Steel fabrication is complete.
- Utility's inverter requirement decision is still pending. Borrego has submitted an alternate, which has been accepted, and procurement is underway.
- Contractor mobilized on 2/22/2021. Perimeter fencing in place.
- Canopy purlins and rebar cages have been delivered.
- Canopy foundation locations have been laid out by the survey team.

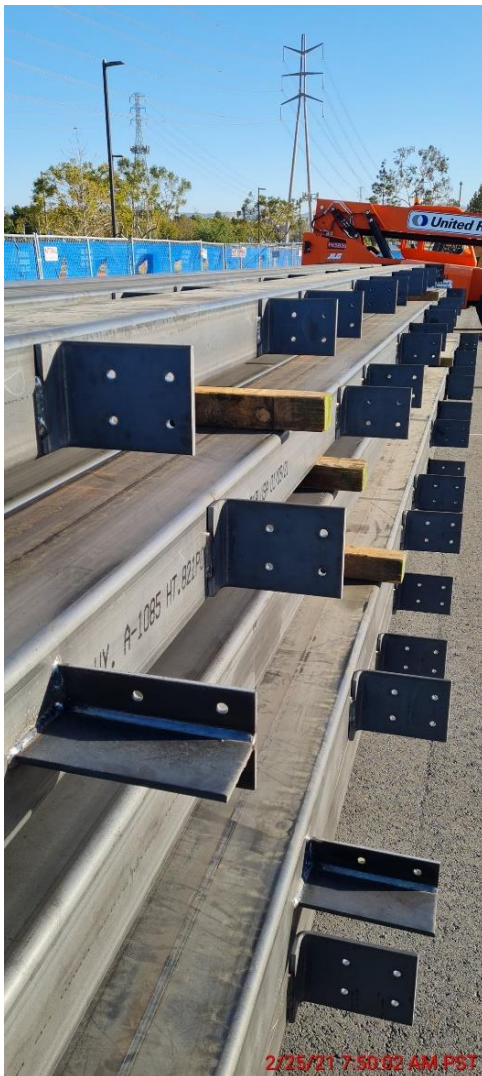

Purlins on Site

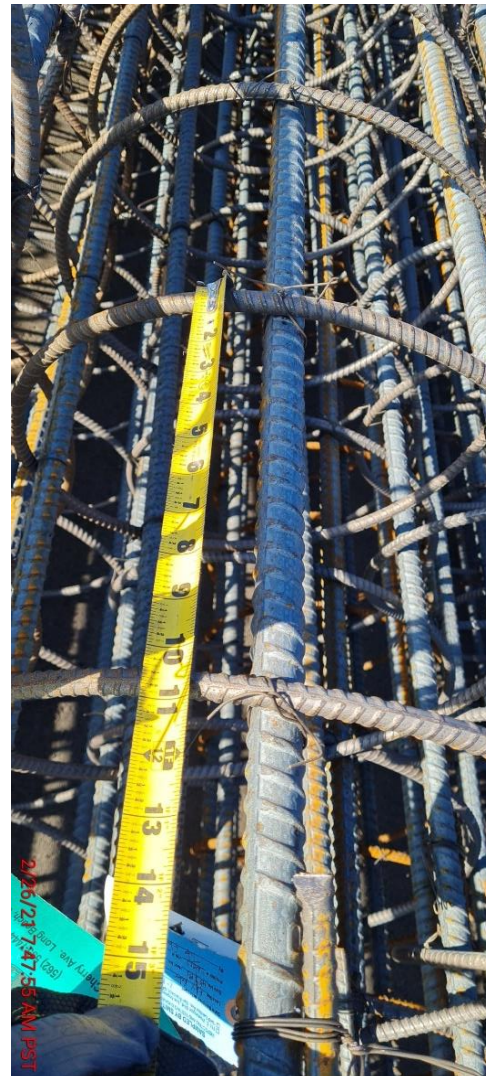

Rebar Cages for Foundations

Upcoming Activities:

- Continuing procurement of equipment.
- Drilling for canopy foundations and concrete placement.
