

FACILITIES PLAN STATUS REPORT
March 23, 2020

CAPITAL IMPROVEMENT PLANNING


The decision to design and construct capital improvement projects begins with the Education and Facilities Master Planning (EFMP) process. The last EFMP cycle was completed December 2011. The 2011 EFMP report is available at the District website: http://www.socccd.edu/about/about_planning.html. The District is in the process of developing a new Education Master and Strategic Plan (EMSP) along with a new Facilities Master Plan. We anticipate these to be complete by the end of this fiscal year. This report contains information on projects over \$1 million that are listed in the Facilities Master Plans for both colleges and projects that include associated planning efforts.

SADDLEBACK COLLEGE

1. STADIUM AND SITE IMPROVEMENT

Project Description: The existing stadium will be replaced with a new 8,000 seat multi-sport stadium with restrooms, team rooms, concession stand, ticket booth, storage, press box, scoreboard, synthetic turf and nine-lane running track. This project includes the southeast campus perimeter drainage control and campus storm water outfall on County of Orange property. The existing practice fields and thrower’s park will be relocated to and replace the Golf Driving Range and expanded to include a soccer practice field.

Start Preliminary Plans	Mar 2014	Award D/B Contract	Aug 2016
Start Working Drawings	Sep 2016	Complete Construction	Jul 2020
Complete Working Drawings	Nov 2017	Advertise for FF&E	Nov 2019
DSA Final Approval	Nov 2018	DSA Close Out	Pending

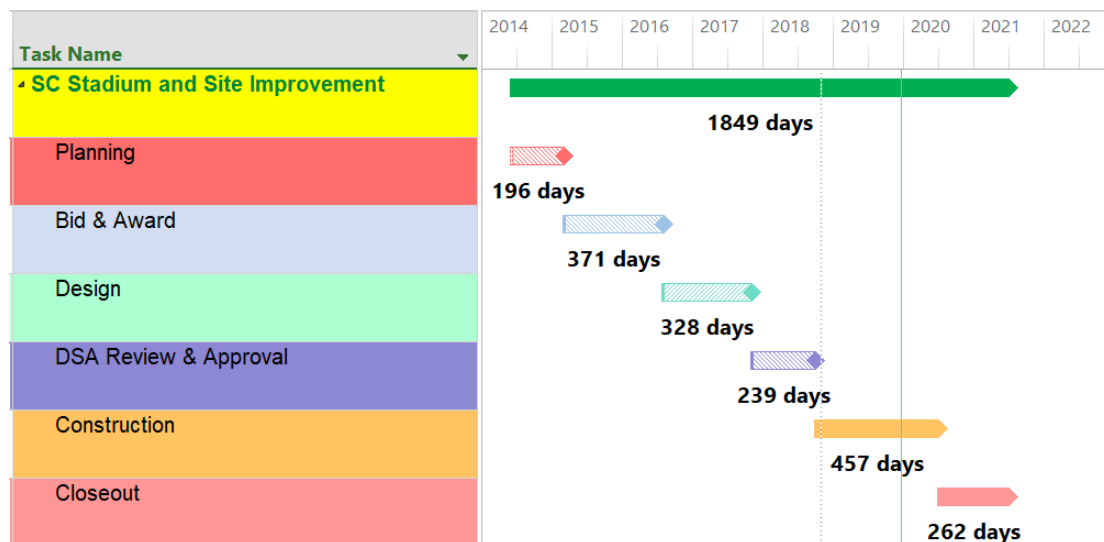

Budget Narrative: Budget reflects Board action on 3/24/2008, 6/23/2014, and 6/22/2015. Several previously budgeted projects are integrated into a single project budget: Upper Quad (2008 - \$1M), Loop Road (2008 - \$3,442,000), Storm Drain Repairs (2013 - \$1,500,000) and Storm Drain, Parking, Practice Fields (2014 - \$7,638,000). On June 23, 2014, the Board approved \$950,000 and on June 22, 2015, the Board approved additional funds of \$7,945,000 and \$17,050,000. The Board approved Saddleback College's use of their RDA funds and a portion of the district-wide apartment income of \$22,705,000.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$14,530,000	\$47,700,000	\$62,230,000
District Funding Commitment	\$14,530,000	\$47,700,000	\$62,230,000
Anticipated State Match:	\$N/A	\$N/A	\$N/A
Basic Aid Allocation:	\$14,530,000	\$24,995,000	\$39,525,000
College Contribution:	\$ 0	\$22,705,000	\$22,705,000

Status: Construction Phase: Project is 74% complete.

In Progress: Bleacher erection, scoreboard installation, site concrete, emergency vehicle access road, interior wall framing and drywall, *painting, installation of ceiling grid, drainage and base for main football field, restroom tile*, interior MEP rough-in, and fabricating elevators.


Recently Completed: *Fine grade for the track, tiling of 1st floor home side restrooms, descope outfall repairs from project, and erection of structural steel to press box level. Transfer of the following to permanent power: new stadium complex, PE 500, Golf Pro Shop and cell tower.*

Focus: Proactively work with the contractor on schedule issues to keep end date on target. Meet with PCL executive team. Review contractor's change order requests and claims; conduct meetings to discuss these.

2. ATAS BUILDING PROJECT

Project Description: The Project includes a new 50,000 gross square feet (GSF) two-story building serving career technical education students. This building will be located at the existing tennis courts facility. Eight new tennis courts (including two striped for pickle ball) will replace the existing six and will be located north of the Village. The college has requested that the existing TAS Building demolition, utility relocation and new parking lot be de-scoped. A connector road and installation of additional parking stalls between the baseball field and the new tennis courts is included.

Start Preliminary Plans	Oct 2017	Award D/B Contract	Aug 2018
Start Working Drawings	Oct 2018	Complete Construction	Aug 2022
Complete Working Drawings	Sep 2019	Advertise for FF&E	Pending
DSA Final Approval	Sep 2020	DSA Close Out	Pending

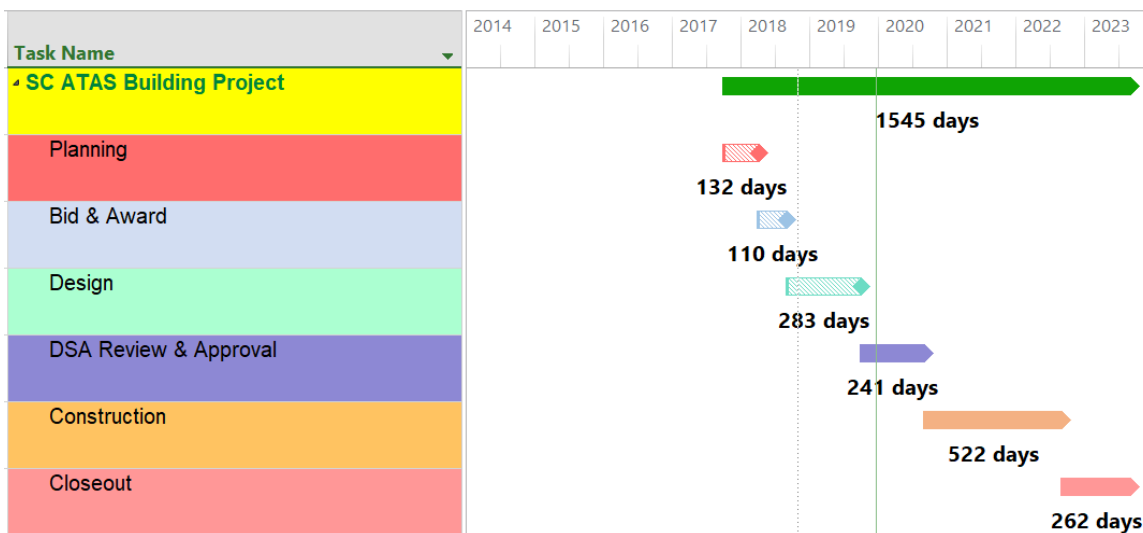

Budget Narrative: In fiscal years 2002-2003 and 2004-2005, \$971,000 and \$985,000 respectively, for a total of \$1,956,000 was allocated from basic aid to cover design. Budget reflects Board action on 8/27/2012, 10/25/2013, 6/23/2014, 8/22/2016 and 5/21/2018. On August 27, 2012, the Board approved \$12,777,313. On October 25, 2013, the Board approved fund reassignment of \$8,523,000 to the Saddleback College Sciences Building. On June 23, 2014, the Board restored \$8,523,000 and added \$2,702,000. On August 22, 2016, the Board approved \$3,110,000. On May 21, 2018, the Board approved \$44,863,622 to fund a new building. The ATAS Building project budget of \$64,100,000 differs from the basic aid allocation due to funds spent for the Technology and Applied Science renovation project prior to the decision to move forward with a new building.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:			
TAS Renovation	\$8,755,055	\$ (7,446,120)	\$ 1,308,935
ATAS Building	\$ 0	\$64,100,000	\$64,100,000
Total	\$8,755,055	\$56,653,880	\$65,408,935
District Funding Commitment:	\$8,755,055	\$56,653,880	\$65,408,935
Anticipated State Match:	\$ 0	\$ 0	\$ 0
Basic Aid Allocation:	\$1,956,000	\$63,452,935	\$65,408,935

Status:

- DSA Review Phase: ATAS Building *back-check* and New Connector Road & Parking Lot 5-B.
- Construction Phase: New Tennis Courts Center (Task #01): Project is approximately 10% complete.

In Progress: DSA *back-check meetings* for the ATAS Building. New Connector Road & parking Lot 5-B documents *resubmittal for back-check process*. *Installation of new underground utilities and building foundations* at the new Tennis Courts Center.


Recently Completed: *Tennis Center grading and existing underground utility re-route. Saddleback College executive cabinet approval on Tennis Center furniture, fixture and equipment list.*

Focus Issue: *Finish Tennis Center underground utilities during spring break. Obtain Moulton Niguel Water District final approval on the New Connector Road & Parking Lot 5-B. Obtain DSA final approval on the ATAS Building and the New Connector Road & Parking Lot 5B Increment No. 1. Kick-off the design process for the baseball field safety netting.*

3. GATEWAY PROJECT

Project Description: This proposed project will construct a new three-story building of 52,156 assignable square feet (ASF), 77,985 gross square feet (GSF) and will provide a new, highly integrated space for student services and consolidated and expanded interdisciplinary instructional space. This project will reduce the need for portable buildings and set the stage for the Student Services building renovation.

Start Preliminary Plans	Sep 2019	Award Construction Contract	May 2021
Start Working Drawings	Jan 2020	Complete Construction	Oct 2022
Complete Working Drawings	Jul 2020	Advertise for FF&E	Feb 2022
DSA Final Approval	Feb 2021	DSA Close Out	Pending

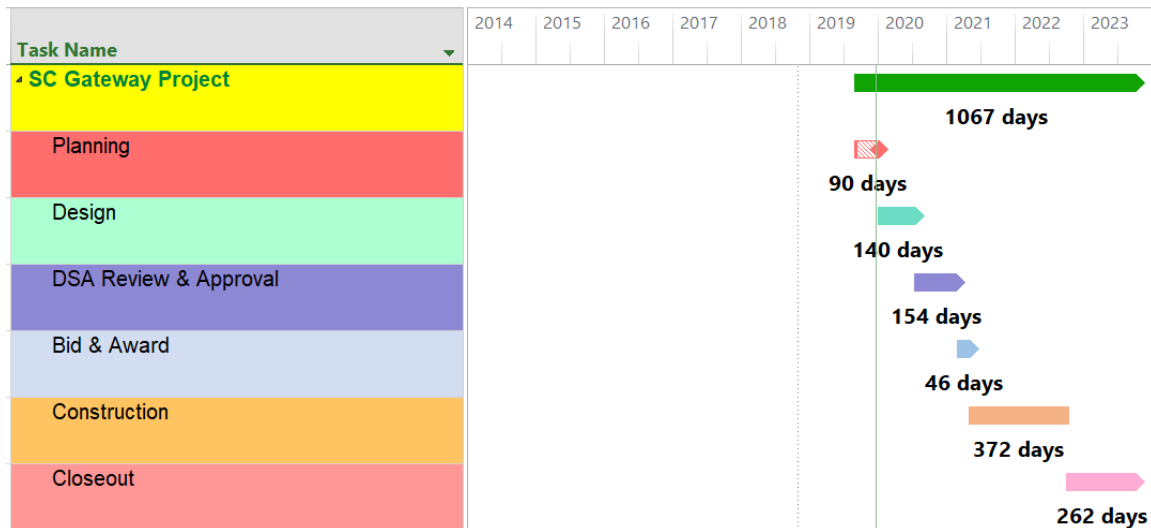

Budget Narrative: Budget reflects Board action on 6/17/2013, 6/23/2014, 8/22/2016 and 6/26/2017 and 4/22/2019. On June 17, 2013, the Board approved \$1,545,115. On June 23, 2014, the Board approved a reduction of (\$655,115). On August 22, 2016, the Board approved \$1,936,817. On June 26, 2017, the Board approved \$16,832,003. On April 22, 2019, the Board approved the funding allocation of \$6,599,180. Request for full funding underway during this FY 2020-2021 funding cycle.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$42,867,000	\$ 8,736,000	\$51,603,000
District Funding Commitment:	\$12,814,000	\$13,444,000	\$26,258,000
State Match:	\$30,053,000	\$ (4,708,000)	\$25,345,000
Basic Aid Allocation:	\$ 1,545,115	\$24,712,885	\$26,258,000

Status: Working Drawings Phase (50% Construction Documents).

In Progress: Weekly Design & Building Information Modeling coordination meetings.


Recently Completed: Saddleback College executive cabinet and stakeholders *sign-off on the 100% Design Development package. Orange County Fire Authority (OCFA) submittal for review & approval. Geotechnical report submittal to Department of Conservation – California Geological Survey (CGS) for final review & approval.*

Focus: Complete Working Drawing Phase and submit 50% Construction Documents to stakeholders for review & sign-off. Kick-off the furniture, fixture and equipment process with Saddleback College executive cabinet.

4. ACCESS CONTROL PROJECT

Project Description: This project will retrofit 1,535 existing doors campus-wide with electronic door locks to provide access control and enhanced safety. This project is similar to the standard established at the Science Building, with hardware synchronized to software monitored by the Saddleback College Campus Police.

Criteria Development	Apr 2018	Award D/B Contract	May 2018
Start Working Drawings	Jun 2018	Complete Construction	Apr 2020
Complete Working Drawings	Jul 2019	FF&E	N/A
DSA Final Approval	Jul 2019	DSA Close Out	Pending

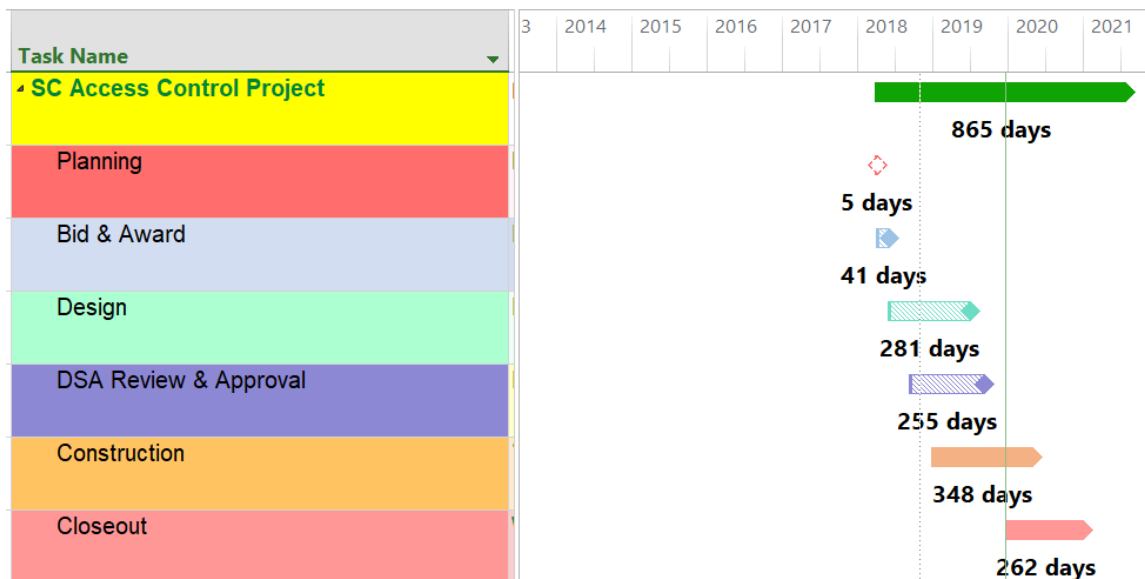

Budget Narrative: Budget reflects the Board action on 6/26/2017 and 5/21/2018. On June 26, 2017, the Board approved \$3,000,000 for the District-wide ADA Transition Plan. Saddleback College assigned \$1,600,000 from its share of the ADA transition funds to this project. On May 21, 2018, the Board approved \$4,000,000. Saddleback College also assigned \$1,364,296 from college general funds. Additionally, State Scheduled Maintenance allocations across FY 2015-16, 2016-2017, 2017-2018 total \$4,845,914.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$11,810,210	\$0	\$11,810,210
District Funding Commitment:	\$ 6,964,296	\$0	\$ 6,964,296
Basic Aid Allocation:	\$ 4,000,000	\$0	\$ 4,000,000
Basic Aid ADA Allocation:	\$ 1,600,000	\$0	\$ 1,600,000
College General Fund:	\$ 1,364,296	\$0	\$ 1,364,296
State Scheduled Maintenance Allocation:	\$ 4,845,914	\$0	\$ 4,845,914

Status: Construction Phase. Phased Project with six increments: Increment No. 1 completed. Increments No. 2 and No.3 (BGS, SSC, HS, AGB, and LRC) are complete. Increment No. 4 construction (Fine Arts & CDC) 85% complete. Increment No. 5 construction (PE Buildings and the Grounds Complex) is underway. Less than 300 doors remain out of 1,535.

In Progress: Increments No. 4 and No. 5 construction.


Recently Completed: Increments No. 2 and No. 3.

Focus: Increment No. 4 (Fine Arts & CDC) and Increment No. 5 (PE Buildings and Grounds Complex) construction.

5. PE RENOVATION

Project Description: This project will renovate the Women’s Locker Room to address Title IX regulations and functional issues, install new rooftop HVAC units on the PE 100 building to correct heating and cooling issues, and renovate the restrooms in PE 300 to meet accessibility requirements.

Start Preliminary Plans	Jul 2019	Award Construction Contract	May 2020
Start Working Drawings	Aug 2019	Complete Construction	Apr 2021
Complete Working Drawings	Dec 2019	Advertise for Equipment	Nov 2020
DSA Final Approval	Mar 2020	DSA Close Out	Pending

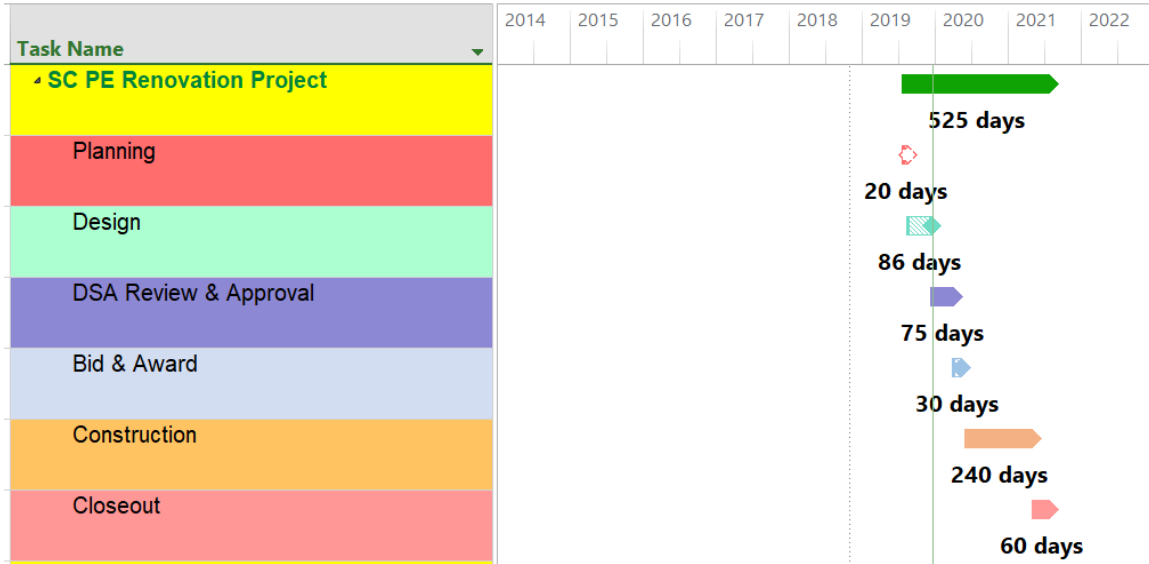

Budget Narrative: Budget reflects Board action on 6/17/2013 and 6/25/2018. On June 17, 2013, the Board approved \$800,000 for the PE 100 HVAC system. Saddleback College contributed \$800,000 in matching funds from the Scheduled Maintenance budget. On June 25, 2018, the Board approved \$1,800,000 for PE Renovation. The college spent basic aid funds of \$211,263 on a previous PE 100 weight-room floor replacement project.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$3,400,000	\$(211,263)	\$3,188,737
District Funding Commitment:	\$3,400,000	\$(211,263)	\$3,188,737
Basic Aid Allocation:	\$2,600,000	\$(211,263)	\$2,388,737
Local Scheduled Maintenance:	\$ 800,000	\$0	\$ 800,000
Anticipated State Match:	N/A		

Status: *Design Phase DSA review.*

In Progress: *Preparing construction phasing plan. Architect preparing for back-check.*

Recently Completed: *Responded to DSA comments.*

Focus: *Prepare bid package.*


IRVINE VALLEY COLLEGE

1. FINE ARTS PROJECT

Project Description: The proposed project will construct three buildings totaling 40,155 assignable square feet (ASF), 57,560 gross square feet (GSF) and will consolidate and expand the Fine Arts department. Art, Art History, Music and Dance instruction will

relocate from laboratories currently housed across a number of different buildings on campus. The Fine Arts buildings, located southwest of the existing Performing Arts Center, will include an assembly space, labs and classrooms with some offices. Space will be vacated within the B-100, B-300 and A-300 buildings for future renovation.

Start Preliminary Plans	Sep 2019	Award Construction Contract	Apr 2021
Start Working Drawings	Jan 2020	Complete Construction	Sep 2022
Complete Working Drawings	Jun 2020	Advertise for Equipment	Jan 2022
DSA Final Approval	Jan 2021	DSA Close Out	Pending

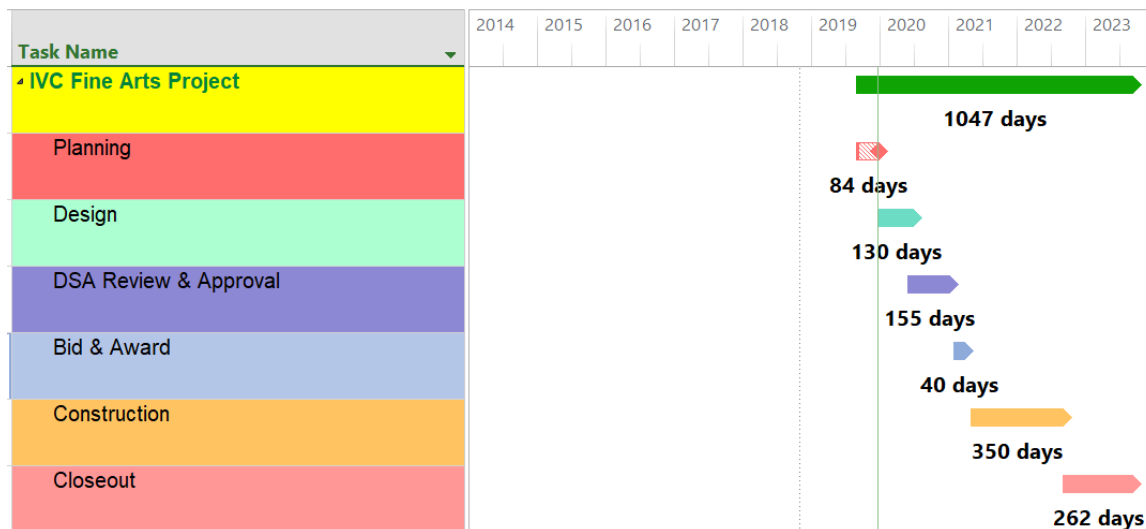

Budget Narrative: Budget reflects Board action on 6/17/2013, 6/23/2014, 8/22/2016, 6/26/2017, and 4/22/2019. On June 17, 2013, the Board approved \$61,278. On June 23, 2014, the Board approved \$795,000. On August 22, 2016, the Board approved \$1,659,739. On June 26, 2017, the Board approved \$12,932,581. On April 22, 2019, the Board approved the funding allocation of \$7,172,680. Request for full funding underway during this FY 2020-2021 funding cycle.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$35,764,278	\$ 9,318,722	\$45,083,000
District Funding Commitment:	\$10,623,278	\$11,998,000	\$22,621,278
State Match:	\$25,141,000	\$(2,679,000)	\$22,462,000
Basic Aid Allocation:	\$ 61,278	\$22,560,000	\$22,621,278

Status: Working Drawings Phase.

In Progress: Design Development documentation.


Recently Completed: Design reviews by commissioning agent and building envelope consultant. Inventory of existing equipment and furniture to be relocated to new building upon completion.

Focus: 50% Construction Documents Phase and presentation to users, facilities and executive staff.

2. PARKING LOT PHASE 1 & 2 AND SOLAR SHADE PROJECT

Project Description: This project includes development of a 190,000 square foot, lighted parking lot creating 594 additional parking spaces. The project includes photovoltaic panels supported on parking canopies and a battery storage system. Both systems will interconnect with the local utility grid and integrate with the campus electrical system, which will be consolidated in response to utility requirements.

Start Preliminary Plans	May 2020	Begin construction	Sep 2020
Start Working Drawings	Jun 2020	Complete Construction	Feb 2021
Complete Working Drawings	Jul 2020	Advertise for FF&E	N/A
DSA Final Approval	Aug 2020	DSA Close Out	Mar 2021

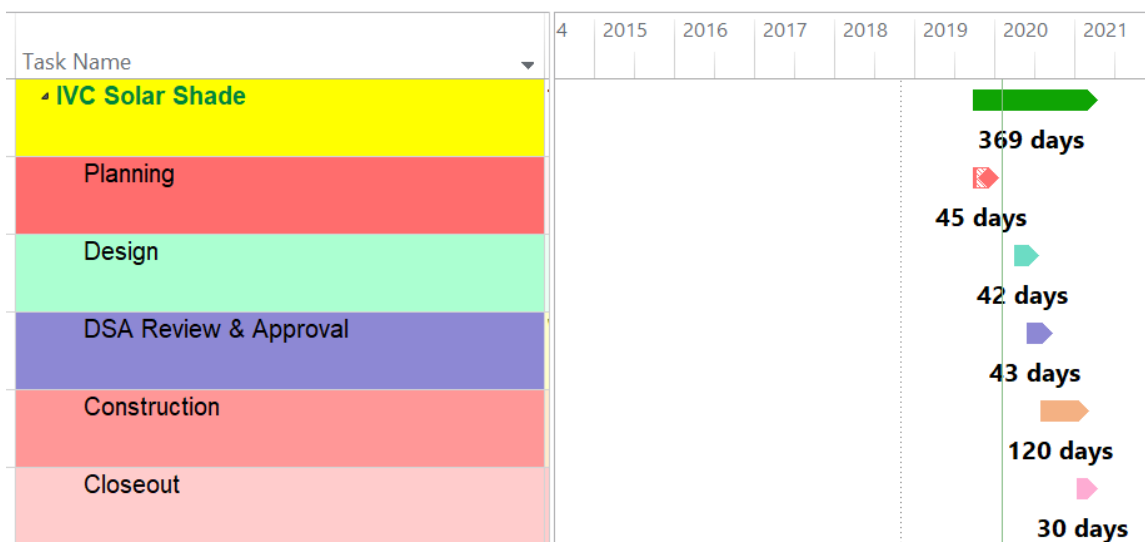

Budget Narrative: Budget reflects Board action on 6/23/2014, 6/22/2015, 8/22/2016, 6/26/2017 and 5/21/2018. On June 23, 2014, the Board approved \$3,010,000. On June 22, 2015, the Board approved \$90,000. On August 22, 2016, the Board approved \$3,655,000 to allow inclusion of the solar shade project and add a connection to the new perimeter road. On June 26, 2017, the Board approved \$733,000. On May 21, 2018, the Board approved \$1,300,000 to include the Phase II parking scope.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$3,010,000	\$5,778,000	\$8,788,000
District Funding Commitment:	\$3,010,000	\$5,778,000	\$8,788,000
Anticipated State Match:	\$N/A	\$N/A	\$N/A
Basic Aid Allocation:	\$3,010,000	\$5,778,000	\$8,788,000

Status: Bid and Award Phase.

In Progress: Contract Negotiation underway.


Recently Completed: Receipt of Solar Shade project bid.

Focus: Negotiate Solar Shade contract.

3. HEALTH CENTER/CONCESSION PROJECT

Project Description: This project is a new one-story building with an estimated 2,214 assignable square feet (ASF), 3,730 gross square feet (GSF) dedicated to Health Center services, Sports Medicine, sports concession and toilet facilities. The Health Center will move from the existing Student Services building. The new Health Center/Concession building is located adjacent to the baseball fields and includes baseball bleacher seating for 300.

Start Preliminary Plans	May 2017	Award Construction Contract	Aug 2018
Start Working Drawings	Jul 2017	Complete Construction	Dec 2019
Complete Working Drawings	Jan 2018	Advertise for Equipment	Jun 2019
DSA Final Approval	Jun 2018	DSA Close Out	Pending

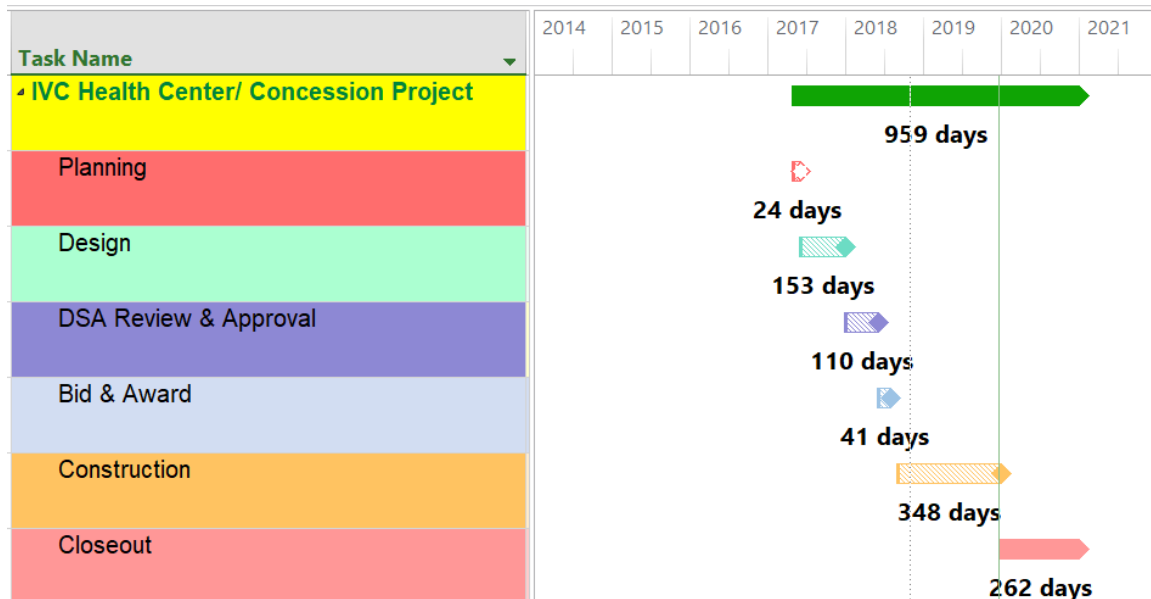

Budget Narrative: Budget reflects Board action on 6/22/2015, 8/22/2016, 6/26/2017 and 5/21/2018. On June 22, 2015, the Board approved \$400,000. On August 22, 2016, the Board approved \$5,338,000. On June 26, 2017, the Board approved \$402,000. On May 21, 2018, the Board approved \$1,360,000.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$5,200,000	\$2,300,000	\$7,500,000
District Funding Commitment:	\$5,200,000	\$2,300,000	\$7,500,000
Anticipated State Match:	\$ 0	\$ 0	\$ 0
Basic Aid Allocation:	\$ 400,000	\$7,100,000	\$7,500,000

Status: Construction Phase: Project is approximately 98% complete.

In Progress: DSA close out.


Recently Completed: Access Control and building dedication.

Focus: DSA close out.

4. STUDENT SERVICES CENTER

Project Description: This project will replace the 30,558 gross square feet (GSF) Student Services Center with two new buildings to correct structural issues, address programming needs, upgrade the food service area, HVAC, electrical, finishes, and provide upgrades to meet ADA requirements. This plan will consolidate all student services into the two buildings with a separate building for food services and student activities.

Start Preliminary Plans	Sep 2019	Award Construction Contract	May 2022
Start Working Drawings	Sep 2020	Complete Construction	May 2024
Complete Working Drawings	Mar 2021	Advertise for Equipment	Aug 2023
DSA Final Approval	Feb 2022	DSA Close Out	Pending

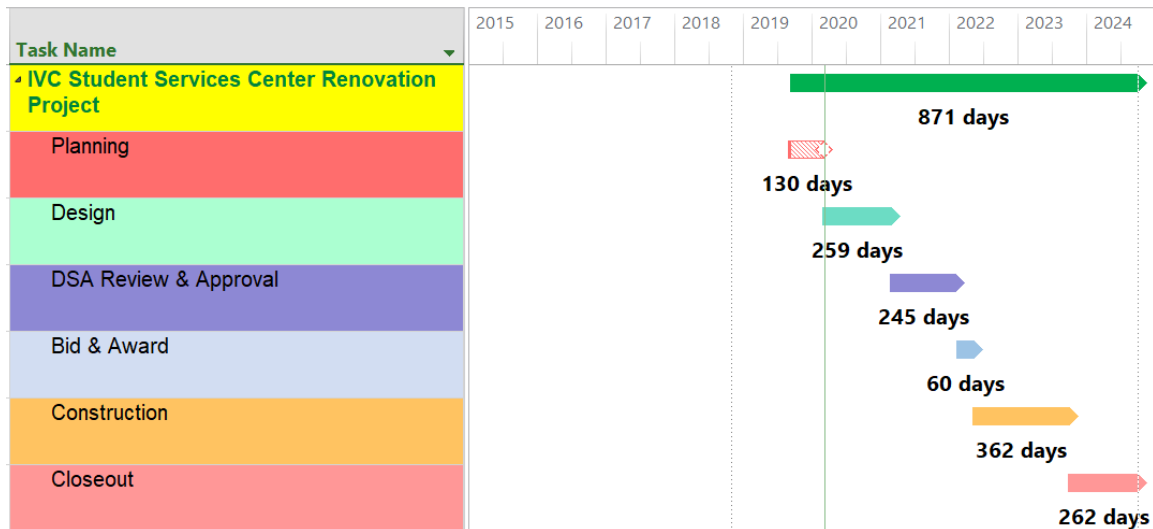

Budget Narrative: Budget reflects Board action on 4/22/2019. On April 22, 2019, the Board approved \$23,850,000.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$90,000,000	\$0	\$90,000,000
District Funding Commitment:	\$48,300,000	\$0	\$48,300,000
Anticipated State Match:	\$N/A		
Basic Aid Allocation:	\$23,850,000	\$0	\$23,850,000

Status: *Schematic Design Phase.*

In Progress: *Schematic Design.*

Recently Completed: *Programming Phase.*


Focus: *Work with end users to further develop design.*

ATEP

1. ATEP - IVC FIRST BUILDING

Project Description: This project is a new two-story 20,249 assignable square feet (ASF), 32,492 gross square feet (GSF) building. The new ATEP IVC First Building consists primarily of lab classrooms with some lecture classroom space, offices and student support services. The building was designed for automation (HAAS), subtractive and additive 3-D sculpting labs, design model prototyping, electronics, photonics, electrical, engineering computer labs, the testing center and some spaces that represent expansion. In addition to the programs identified during design, a portion of the Adult ESL (English as a second language) and the Emeritus and Community Education offices were moved to the ATEP IDEA building at its opening. The project includes 50kW of solar electric power and is a LEED Gold Equivalent building.

Start Preliminary Plans	Oct 2014	Award D-B Contract	Jun 2015
Start Working Drawings	Jul 2015	Complete Construction	Mar 2018
Complete Working Drawings	Mar 2016	Advertise for FF&E	Sep 2017
DSA Final Approval	Sep 2016	DSA Close Out	Aug 2018

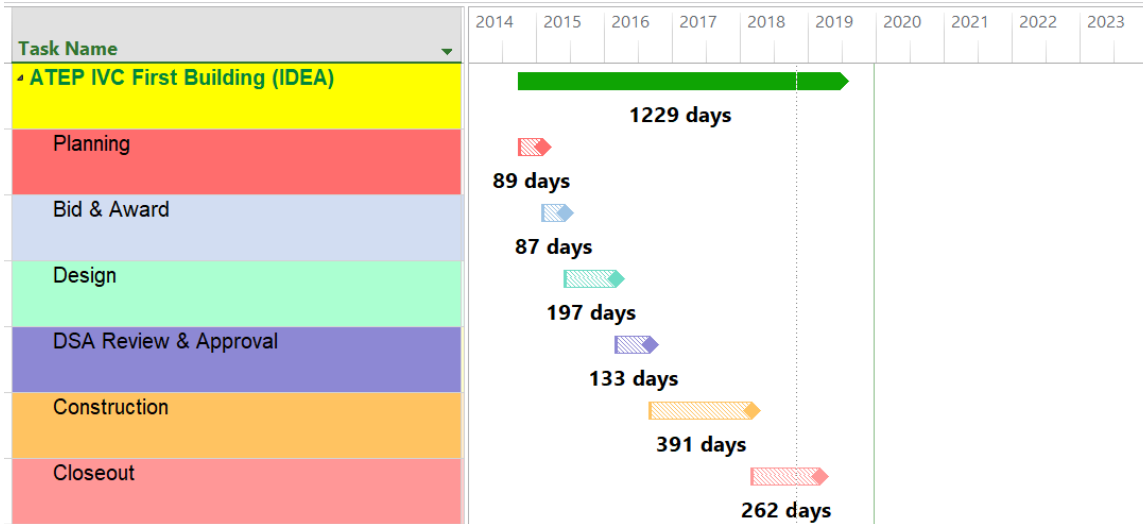

Budget Narrative: Budget reflects Board action on 2/28/2011, 6/23/2014, 6/22/2015, 8/22/2016 and 6/26/2017. On February 28, 2011, the Board approved \$12,500,000, originally allocated to the Phase 3A project budget and transferred to the IVC ATEP First Building with \$8,950,000 additional funds Board approved on June 23, 2014. On June 22, 2015, the Board approved \$3,250,000 for associated parking. On August 22, 2016, the Board approved the FF&E budget of \$1,600,000. The college applied Irvine Valley College RDA funds equaling \$1,250,000 for an expanded lobby and \$700,000 for additional IT equipment. On June 26, 2017, the Board approved \$1,100,000.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$23,000,000	\$ 6,350,000	\$29,350,000
District Funding Commitment:	\$23,000,000	\$ 6,350,000	\$29,350,000
Anticipated State Match:	\$ 0	\$ 0	\$ 0
Basic Aid Allocation:	\$21,450,000	\$ 5,950,000	\$27,400,000
College Contribution:	\$ 0	\$ 1,950,000	\$ 1,950,000

Status: Project close out.

In Progress: Coordinate with contractor and SCE for battery storage Permission to Operate (PTO). Coordinate warranty related items with contractor.

Recently Completed: Execution of new interconnect agreement with SCE for combined battery storage and photovoltaic system.


Focus: Work through system commissioning with SCE to “go live”. Continue discussions with contractor to address end users’ first-year discovery warranty items.

2. ATEP – SIGNAGE PROJECT

Project Description: Wayfinding signage for ATEP consists of three monument signs, five vehicle signs and one pedestrian sign. This signage will define the campus as a destination,

support route planning, clarify entrances and parking, create a main pathway, and establish a standardized naming system.

Start Preliminary Plans	Mar 2017	Award Construction Contract	Nov 2019
Start Working Drawings	Aug 2018	Complete Construction	June 2020
Complete Working Drawings	Apr 2019	Advertise for FF&E	N/A
DSA Final Approval	Aug 2019	DSA Close Out	July 2020

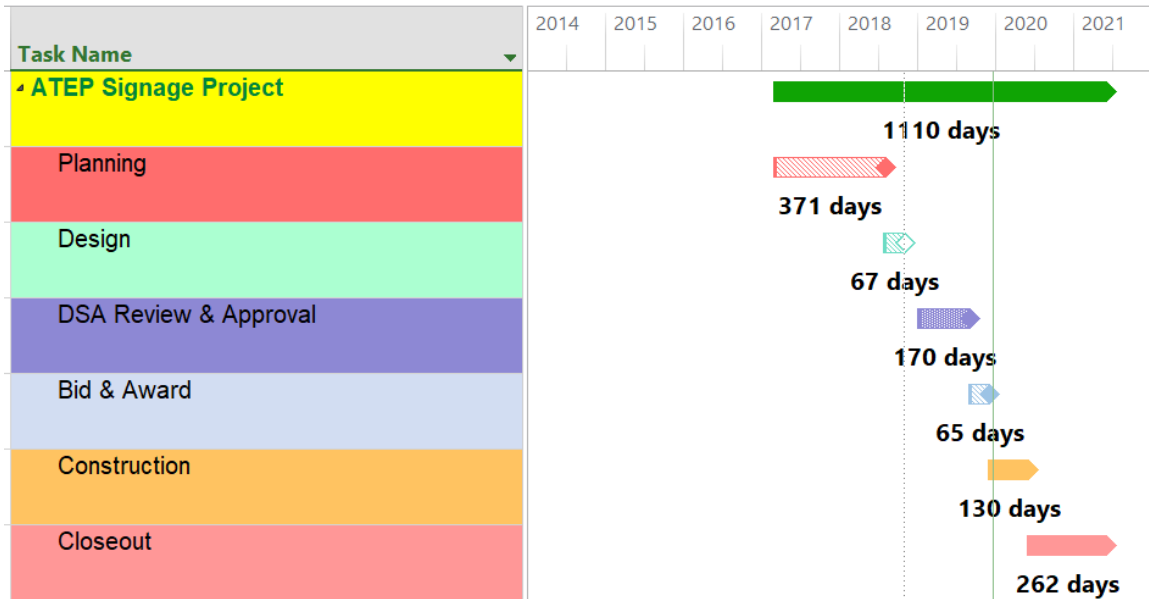

Budget Narrative: Budget reflects Board action on 5/21/2018 and 4/22/2019. On May 21, 2018, the Board approved \$500,000. On April 22, 2019, the Board approved the funding allocation of \$4,431,121.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$3,000,000	\$1,931,121	\$4,931,121
District Funding Commitment:	\$ 500,000	\$4,431,121	\$4,931,121
Anticipated State Match:	\$ 0	\$ 0	\$ 0
Basic Aid Allocation:	\$ 500,000	\$4,431,121	\$4,931,121

Status: Construction Phase: Project is approximately 15% complete.

In Progress: District review and approval of signage submittal. Sign footing excavation. Install underground electrical pull boxes.

Recently Completed: Parking lot and boring locations backfill and asphalt patch.


Focus: Layout, excavate and form monument signs at roundabouts and main campus entrance.

DISTRICT WIDE

1. MAPPING AND CONDITION ASSESSMENT

Project Description: This project comprehensively documents the horizontal and vertical positions of underground utilities and assesses existing conditions. Accurate utility information prevents construction delays, claims, and utilities conflicts.

Kick Off	Aug 2018	Start Plan Development	Aug 2018
Start Research/Analysis	Aug 2018	Draft Plan	Mar 2019
Complete Research/Analysis	Mar 2019	Final	Jan 2021

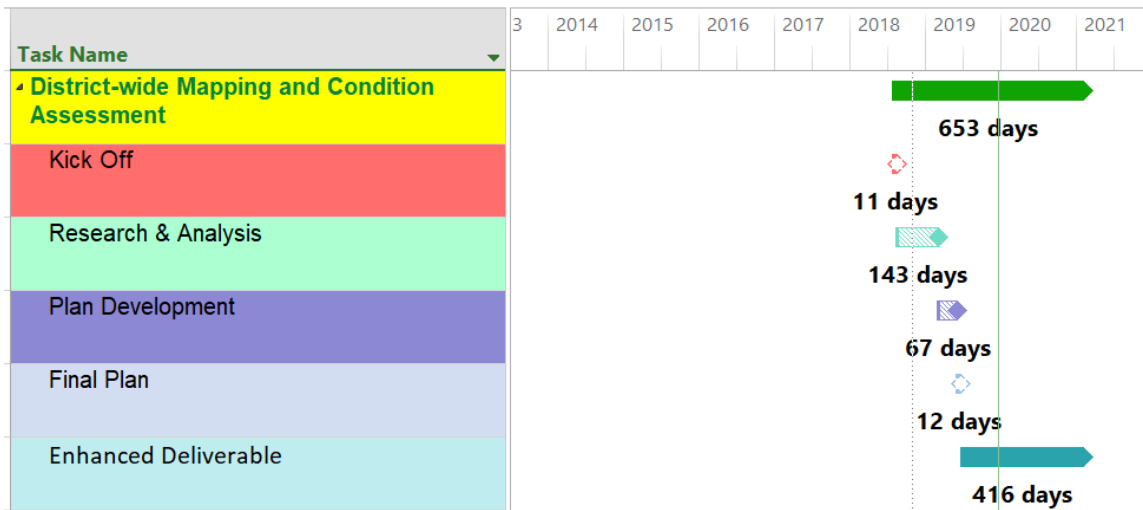

Budget Narrative: Budget reflects Board action on 8/22/2016, 6/26/2017, and 5/21/2018. On August 22, 2016, the Board approved \$400,000. On June 26, 2017, the Board approved \$500,000. On May 21, 2018, the Board approved \$3,000,000.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$400,000	\$3,500,000	\$3,900,000
District Funding Commitment:	\$400,000	\$3,500,000	\$3,900,000
Anticipated State Match:	\$N/A	\$N/A	\$N/A
Basic Aid Allocation:	\$400,000	\$3,500,000	\$3,900,000

Status: Phase Five (Enhanced Deliverables at Saddleback, IVC and ATEP). *This project will be removed from future reports.*

In Progress: *Field survey at ATEP.*


Recently Completed: *Finalize scope for ATEP parking lot Underground Utility Assessment.*

Focus: Finalize ATEP *scope and* verify fire lane condition to support the Fine Arts Complex project.

2. ARCHITECTURAL STANDARDS

Project Description: The District-wide Standards will provide all future capital projects with design and construction consistency, operational efficiency, maintainability, accessibility and sustainability while ensuring first class teaching and learning facilities. These standards will be developed to promote the efficient, predictable, and cost-effective design and construction of all new and modernized facilities, will represent the best value for District expenditures, and will align with the District’s long-range goals. The standards will include sections on the 2020 Facilities Master Plan, ATEP Design Standards, Infrastructure Master Plan, Landscape Master Plan, Storm Water Management Plan, Signage and Wayfinding Standards, Easement Plan, Blue Phone/Emergency Plans, Building Information Modeling Standards (BIM), Design Guidelines for offices, classrooms, furniture standards, restrooms, interior building and exterior circulation, and utility rooms, Building Systems Guidelines and Technical Standards and Guidelines.

Kick Off, Phase II	Feb 2020	Start Plan Development	TBD
Start Research/Analysis	Feb 2020	Complete Plan	Jun 2021
Complete Research/Analysis	TBD	Final Plan, Phase II	Jun 2021

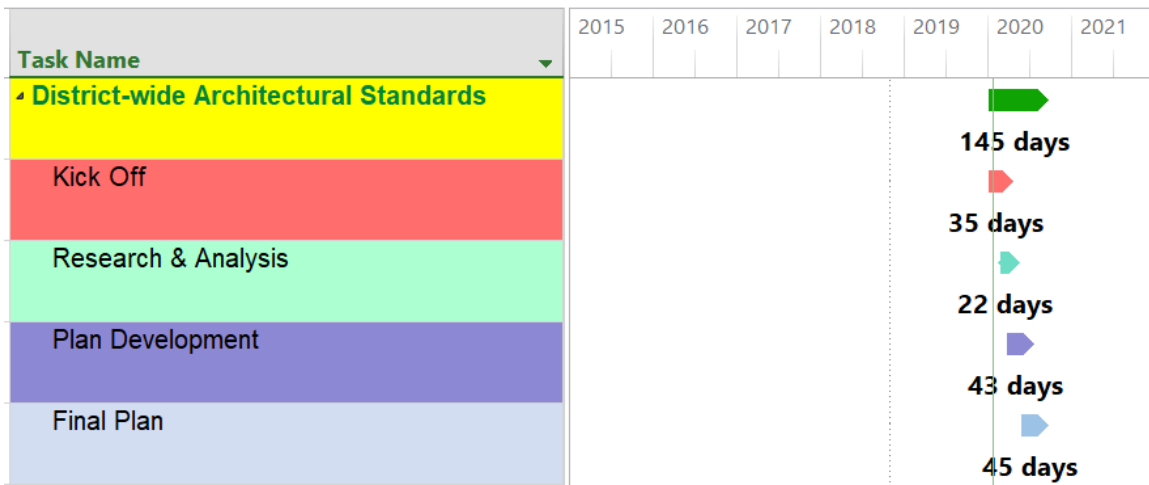

Budget Narrative: On April 22, 2019, the Board of Trustees approved \$1,500,000 for the Architectural Standards project.

	<u>Original</u>	<u>Revision</u>	<u>Total</u>
Project Budget:	\$1,500,000	\$0	\$1,500,000
District Funding Commitment:	\$1,500,000	\$0	\$1,500,000
Anticipated State Match:	\$N/A	\$N/A	\$N/A
Basic Aid Allocation:	\$1,500,000	\$0	\$1,500,000

Status: Research and Analysis Phase.

In Progress: *Classroom design standard review. Establish committees for landscaping and storm drainage.*

Recently Completed: *Finalize responsibility matrix for all scopes to be included in the document. Attend meetings of existing college committees to be able to tie efforts together.*

Focus: Set appropriate foundation. Define committee responsibilities.

GENERAL NOTES

- Project updates for active projects may be viewed at:
<http://www.socccd.edu/businessservices/ProjectUpdates.html>
- Schedule Table: Bold dates in the schedule table indicate actuals. Items that are not bold indicate anticipated dates.
- Budget Table:
 - When state matches are identified, the project budgets reflect the allocated state match as reported in FUSION for the latest planning year. (FUSION is the State Chancellor’s Office database for Capital Outlay.)
 - The “Revisions” column for the State Match category includes changes due to escalation and changes that may have occurred to the state’s percentage (i.e. going from an 80% match down to a 50% match) as the economy has changed from the original project approvals to current date. The “Revisions” column for the Basic Aid Allocation will show a total variation to date taking into account both increased and decreased basic aid allocations.
 - The Unassigned category identifies an underfunded budget.
- The Budget Narrative paragraph for each project discusses the history of change to all category amounts over the life of the project.
